

✓	Achieved
😊	On track
😐	Progressing
😞	Not on track
👉	Handover to BAU

Approved by Recovery Manager Barbara Dempsey
Week ending: 31 January 2018

Reconnect our Community (Tuhononga)

COMMUNITY

Highlights for the month

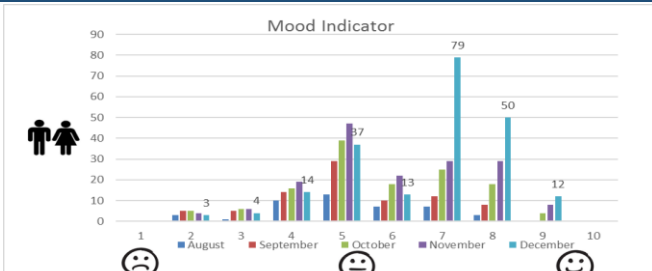
- 169 families from moderately affected (yellow) houses have had repairs completed and are able to move back home.
- 135 Welcome Home Packs have been distributed to residents who have returned home.
- Navigators continue to make contact with flood affected families to provide support. The main issues are health & wellbeing. Additional building advisory support is available to those families who are undertaking or managing their own home rebuilds.
- MBE temporary housing update: There is 1 household waiting for a porta cabin; and 5 families awaiting rental properties.
- The residential advisory service (RAS) saw clients at Te Tari Awhina over a 2-day period in December; with a further visit scheduled in early February. RAS anticipate completion by mid February.
- The 45th Recovery Newsletter will be the final published in the Whakatane Beacon. Fortnightly newsletters will continue to be produced and distributed via the mailchimp database, Recovery webpage and Facebook. Residents who do not have email access have been offered a postal delivery and hard copies will continue to be available from Te Tari Awhina – Community Hub at Edgumbe Library.



Emerging Issues/Risks	Action	Person to action
The target was "90% of affected families/whanau are back in their homes by Christmas 2017". The actual return is just over half of this target. The limitations and rebuild timeframes have been influenced by: weather, insurer and owner agreement timelines, technical repair issues for some land and houses, home owners after cash settlements then arranging own works, actual practical rebuild timeframes, and trades works peaks. Christmas also saw a slow down in rebuild.	The actual returned home status and drivers for rebuild schedules are key monitoring requirements. This ongoing understanding allows existing and new strategies to be implemented such as: building advisory service for home owners undertaking or arranging own works, navigator support for at risk families, and simple touch base with people to check progress and offer any support.	WRO

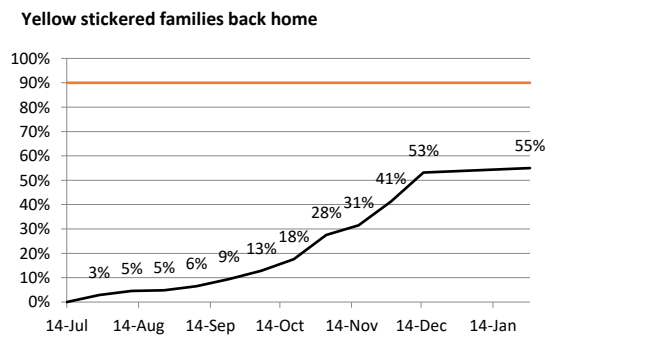
Project Status

Welfare and Wellbeing

Milestones planned for this period	Timeframe	Status	Update on progress
Community Hubs established in Edgumbe, Kawerau, Murupara and Whakatane.	May/June	✓	
Psycho-social recovery plan is developed, agreed and implemented.	June 2017 & ongoing	✓	
Research, development and successful implementation of a 'fit for purpose' navigator service.	June 2017 & ongoing	✓	
Community partners made up of local authorities, iwi and central government agencies convene and collaborate on joined up wrap around service delivery for the wellbeing of affected residents.	July 2017 & ongoing	✓	
Services to the community are developed which outlines a range of reactive and proactive strategies.	June 2017 & ongoing	😊	

Community

Home by Christmas

Milestones planned for this period	Timeframe	Status	Milestones planned for this period	Timeframe	Status
Perception survey on safety returns back to pre-flood levels within 2 years.	2019	👉	Process developed to monitor the repair progress.	June 2017	✓
Property values readjust within 3 years.	2020	👉	"Welcome home" packs developed.	June 2017	✓
List of communication groups & clubs opening and closing demonstrate continuity.	August 2017	✓	At least 90% of affected families/whanau available are back in their homes by Christmas 2017 (refer comments in issue/risk section).	90% by Christmas 2017 (actual 55% at 1 Feb 2017)	😞
A calendar of monthly events and community development activities has been planned out to reach a wide range of the community, including school holiday care programme.	June 2017	✓	Process agreed for managing donated goods.	June 2017	✓
Community expo's and open days will be held to provide timely information to affected residents on a range of topics (e.g. insurance, health, Liveable Homes Project, Worksafe etc)	May 2017 June 2017 September 2017	✓			
Community group develops Community Plan with WDC support.	Commence September 2017	✓			
A community engagement plan is developed and implemented.	June 2017	✓			
An iwi engagement plan is finalised and implemented.	July 2017	✓			
Community acknowledge or commemorate event in a way that the community deems appropriate.	Feb 2018	😊			
Ongoing use of the community leaders group.	Ongoing	✓			
Volunteer coordinator is in place; process to connect work with volunteers is developed and the donation of appropriate materials is sought.	July 2017 Ongoing	✓			

Restoring the Natural & Rural Environment (Whakahou)

NATURAL AND RURAL

Highlights for the month

- College Road Stopbank Realignment: Demolition and house removal work has commenced. Overall, works are scheduled to be substantially complete in May/June.
- A draft regional economic impact assessment report on the rural impact of the floods has been completed by MPI.



Project Status

Primary Sector Support

Environmental Effects

Milestones planned for this period	Timeframe	Status	Milestones planned for this period	Timeframe	Status
Recovery Action Plan developed for rural sector.	September 2017	☹️	Respond to complaints within 3 working days.	Ongoing	✓
Clean up of rural properties complete.	December 2017	😊	All complaints investigated.	Ongoing	✓
A range of reactive and proactive strategies to engage affected rural individuals and families and build strong support networks are provided, including: Good yarn workshops, Local BBQs, Dairy NZ discussion groups, Rugby bus trip, Field days and Ladies morning teas.	Ongoing	✓	Compliance monitoring occurs as set out in schedule 1A and 2A of the BOPRC Resource Management Act and Building Act Charges Policy.	Ongoing (determined by consent)	✓
Workshops for affected farmers delivered (topics: farm management, animal health, soils, agronomy, wellness etc.).	Ongoing	✓	Stakeholder perception survey demonstrates greater than 75% satisfactory involvement in environmental issues.	November 2017	☹️
No flood related cases are outstanding.	Ongoing	😊	Clear messaging is delivered to the rural	May 2017	✓
Positive Regional Economic Quarterly Reports.	December 2017	😊	All amenity areas are open and accessible.	June 2017	✓
Outreach to affected rural properties is no longer flood related.	2019	✓	Site assessments for impact on biodiversity are completed.	October 2017	👋
Land use management advice provided to landowners.	October 2018	👋	If required, recommendations for remediation are received.	December 2017	👋
MPI funding round is successfully taken up by affected rural properties.	September 2017	✓	Biosecurity plans, if appropriate.	December 2017	👋
			Erosion assessment of pre and post river banks.	August 2017	✓
			Urgent erosion sites are repaired.	August 2017	👋
			Damaged sites are repaired.	2020	👋

Repairing our homes and restoring our communities (Waihanga)

BUILT



Highlights for the month

- Liveable Homes Project is now complete: 15 families now back home

Project Status

Housing

Milestones planned for this period	Timeframe	Status	Update on progress							
Chemical contamination testing of silt.	June 2017	✓	<p>Status of building consent applications</p>							
Clean-up of silt complete (sections).	end July 2017	✓								
Clean up of silt complete (under housing).	August 2017	✓								
Asbestos removed safely from all affected properties.	June - July 2017	✓								
Education and training sessions provided.	June - July 2017	✓								
Portacabins sited on private properties.	July 2017	✓								
Portacabins available in Whakatāne Holiday Park.	July 2017	✓								
Other temporary housing options are investigated.	August 2017	✓								
Liveable Homes Project complete by November 2017.	November 2017 (actual Jan 2018)	✓								
People back in homes – 90% by Christmas. (refer comments in issues/risk at beginning of report)	90% by Christmas 2017 (actual 55% at 1 Feb 2017)	☹					Building assessment summary	Red (severe damage)	Yellow (moderate damage)	White (light / no damage)
Insulation component of Liveable Homes Project complete.	October 2017	✓					Edgecumbe urban	15	257	221
Insulation for non-Liveable Homes Project homes is complete.	90% by December 2017	👉					Plains incl. Poroporo	0	41	9
Investigate demand for future residential land in Edgecumbe.	September 2017	😊					Tāneatua / Rūātoki	0	11	2

Reasons for significant variances from plan

The target of "People back in homes – 90% by Christmas" is not achieved. The actual return is just over half of this target as at 31 January 2018. The rebuild timeframes have been influenced by: weather, insurer and owner agreement timelines, technical repair issues for some land and houses, home owners after cash settlements then arranging and scheduling own builders and works, actual practical house drying then rebuild timeframes, and trades works peaks. Christmas period also saw a slow down in rebuild.

Infrastructure

Milestones planned for this period	Timeframe	Status	Milestones planned for this period	Timeframe	Status
THREE WATERS			ROADING		
Three waters infrastructure is fully functioning (BAU).	May 2017	✓	All roads are open (temporary solutions).	August 2017	✓
All temporary infrastructure removed.	December 2017	✓	Horomanga Bridge (temporary bridge installed).	20 July 2017	✓
Investigate future protection of Edgecumbe and Tāneatua wastewater ponds in the LTP.	June 2018	☹	Horomanga Bridge (permanent repair).	design commencing, construction to start approx. Oct 2018	👉
Repair of community facilities are complete.	May 2017	✓	Kopuriki Road reopened.	Mid May 2017	✓
RIVER CONTROL MEASURES			Te Whāiti Road reopened.	7 July 2017	✓
Independent review of the stop bank breach is complete.	End July 2017	✓	Te Whāiti Road – less complex damaged sites repaired.	End August 2017 - (construction underway - completion end of Feb 2018)	👉
Geotechnical investigations.	July 2017	😊	Te Whāiti Road – complex sites requiring investigation & design complete. - (13 complex sites under preconstruction)	May 2018 - (construction commencing Oct/Nov 2018)	👉
Site clearance works.	underway as at Jan 2018	☹	Galatea Road – Te Mahoe underslip – opened to single lane access.	End April 2017	✓
Reinstatement commences.	October 2017 (scheduled March 2018)	☹	Galatea Road – Te Mahoe underslip – 2 lanes reinstated. - tenders closed -	November 2017 - construction to commence Mar 2018	👉
Planning consents.	November 2017 (ongoing)	☹	Pekatahi Bridge reopened.	16 June 2017	✓
Long term future of severely affected area through community plan.	March 2018	😊	SH2 (Waimana Gorge) reopened.	23 June 2017	✓
Stopbank Works on College Road, Edgecumbe are completed.	June 2018	😊	AMENITY AND COMMUNITY VISION		
Stopbank repairs complete.	End March 2018 (subject to consents & other planning)	☹	Community group develops Community Plan with WRO support.	September 2017	✓
College road renewed.	June 2018	😊	Works complete to re-establish amenity in Edgecumbe and other areas.	Commence September 2017	☹

ECONOMY

Highlights for the month

• The \$20,000 MBIE-funded 'Edgecumbe Back in Business' marketing campaign continues across local media organs. Radio campaigns commenced in December for businesses already operating, with a second wave in January. The campaign timeframe was extended, largely due to delays in repairs to Riverslea Mall. The print aspect is anticipated to commence from late January to coincide with businesses returning to Riverslea Mall. Feature pages are booked for 16 and 23 Feb, 9 and 16 March.



Project Status

Business Continuity

Milestones planned for this period	Timeframe	Status
Business needs assessment carried out.	July 2017	✓
Outreach to affected businesses by phone and visits.	July 2017	✓
Fact sheets and web page for business recovery.	July 2017	✓
Business networking and training held to support and assist affected businesses.	July 2017 (ongoing)	✓
Monitor any business closures.	May 2017	✓
Seminars and workshops to provide information and advice.	July 2017 (onwards)	☹
MBIE funding round is successfully taken up by affected businesses.	September 2017	✓
Networking and supporting events are planned and held on fortnightly basis.	May 2017 (ongoing)	☺
"Buy Local" campaign plan.	July 2017	☹
Recovery newsletter on Edgecumbe open for business.	July 2017	☹
Advertising implemented (e.g. radio, newspaper, other).	July 2017	☹
Free wifi in Edgecumbe investigated and installed if possible.	August 2017	✓
Scoping report on economic opportunities developed.	October 2017	☺

MBIE Business Recovery Grant Panel Fund

	New Applications reviewed	Applications approved	Applications Withdrawn	Applications Declined	Applications that did not supply info	Dollar value of applications approved	Potential Applications in the pipeline
Latest panel: 15 December	0	1	0	0	0	\$ 38,851.55	0
In total	25	16	2	5	2	\$ 202,919.05	0
